


Gilmer ISD High School

850 Buffalo Street
Gilmer, Tx 75644




RLM General Contractors

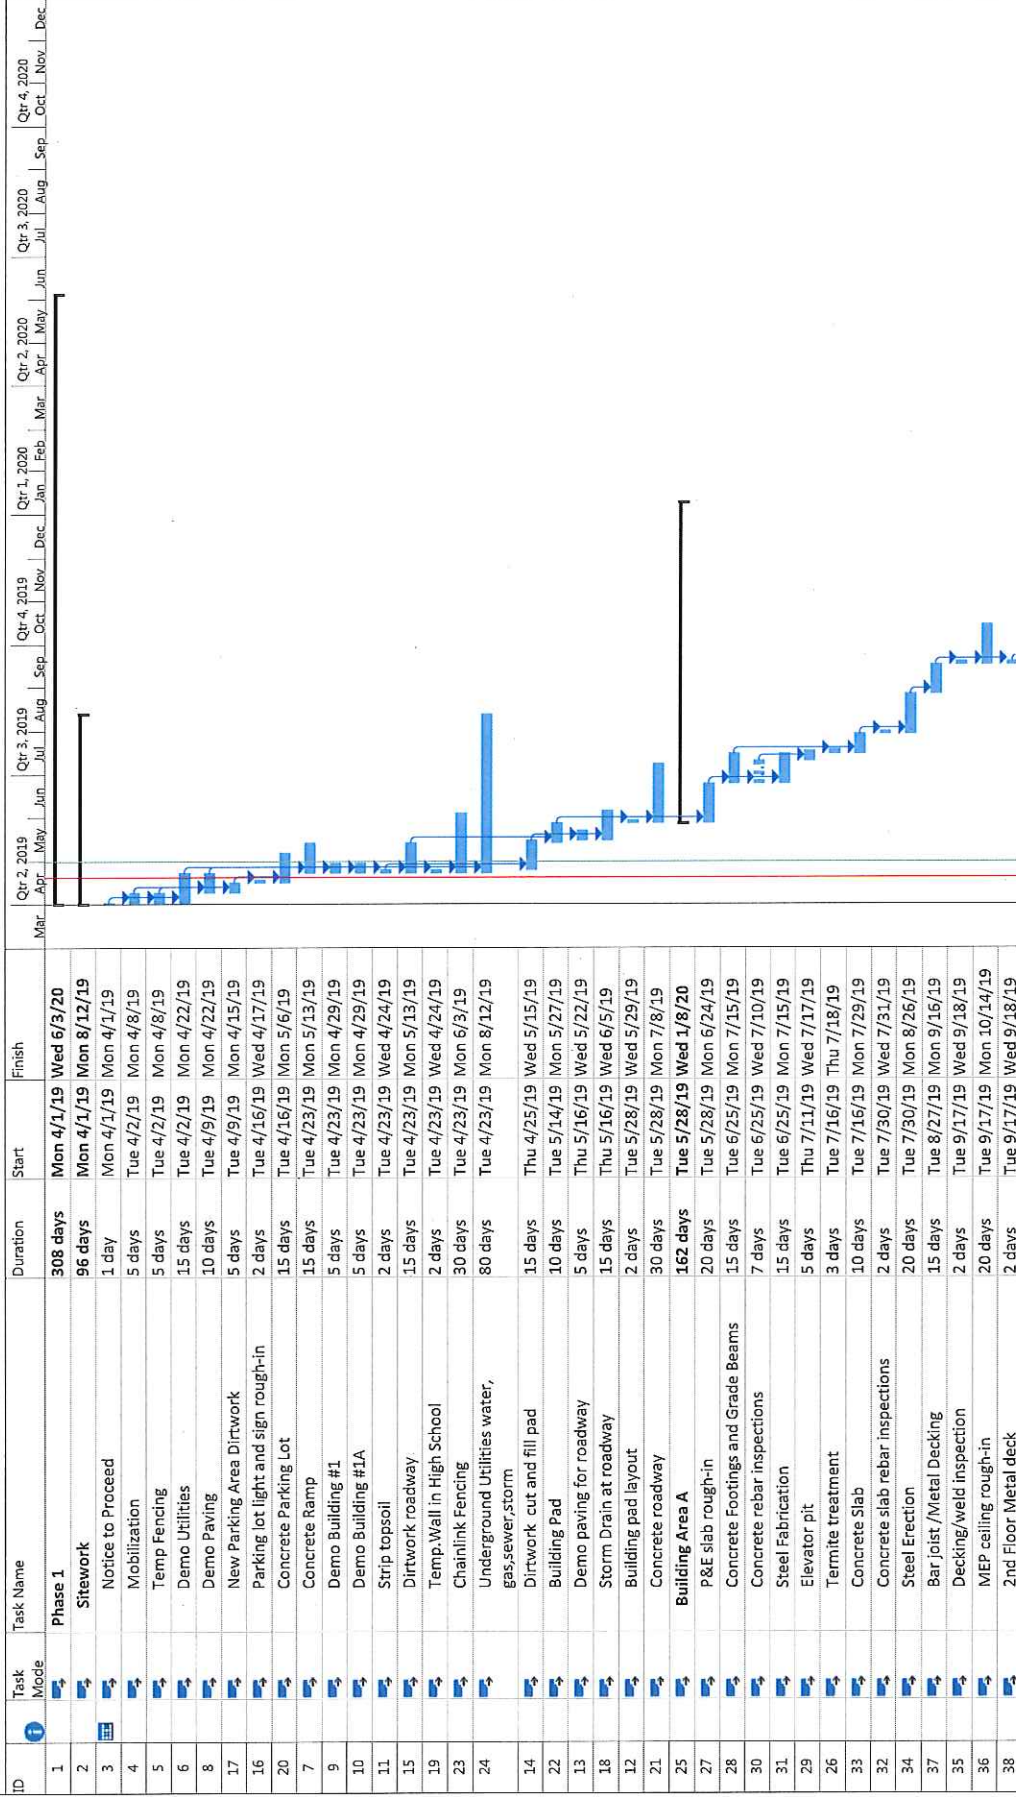

Gilmer ISD High School

850 Buffalo Street
Gilmer, Tx 75644

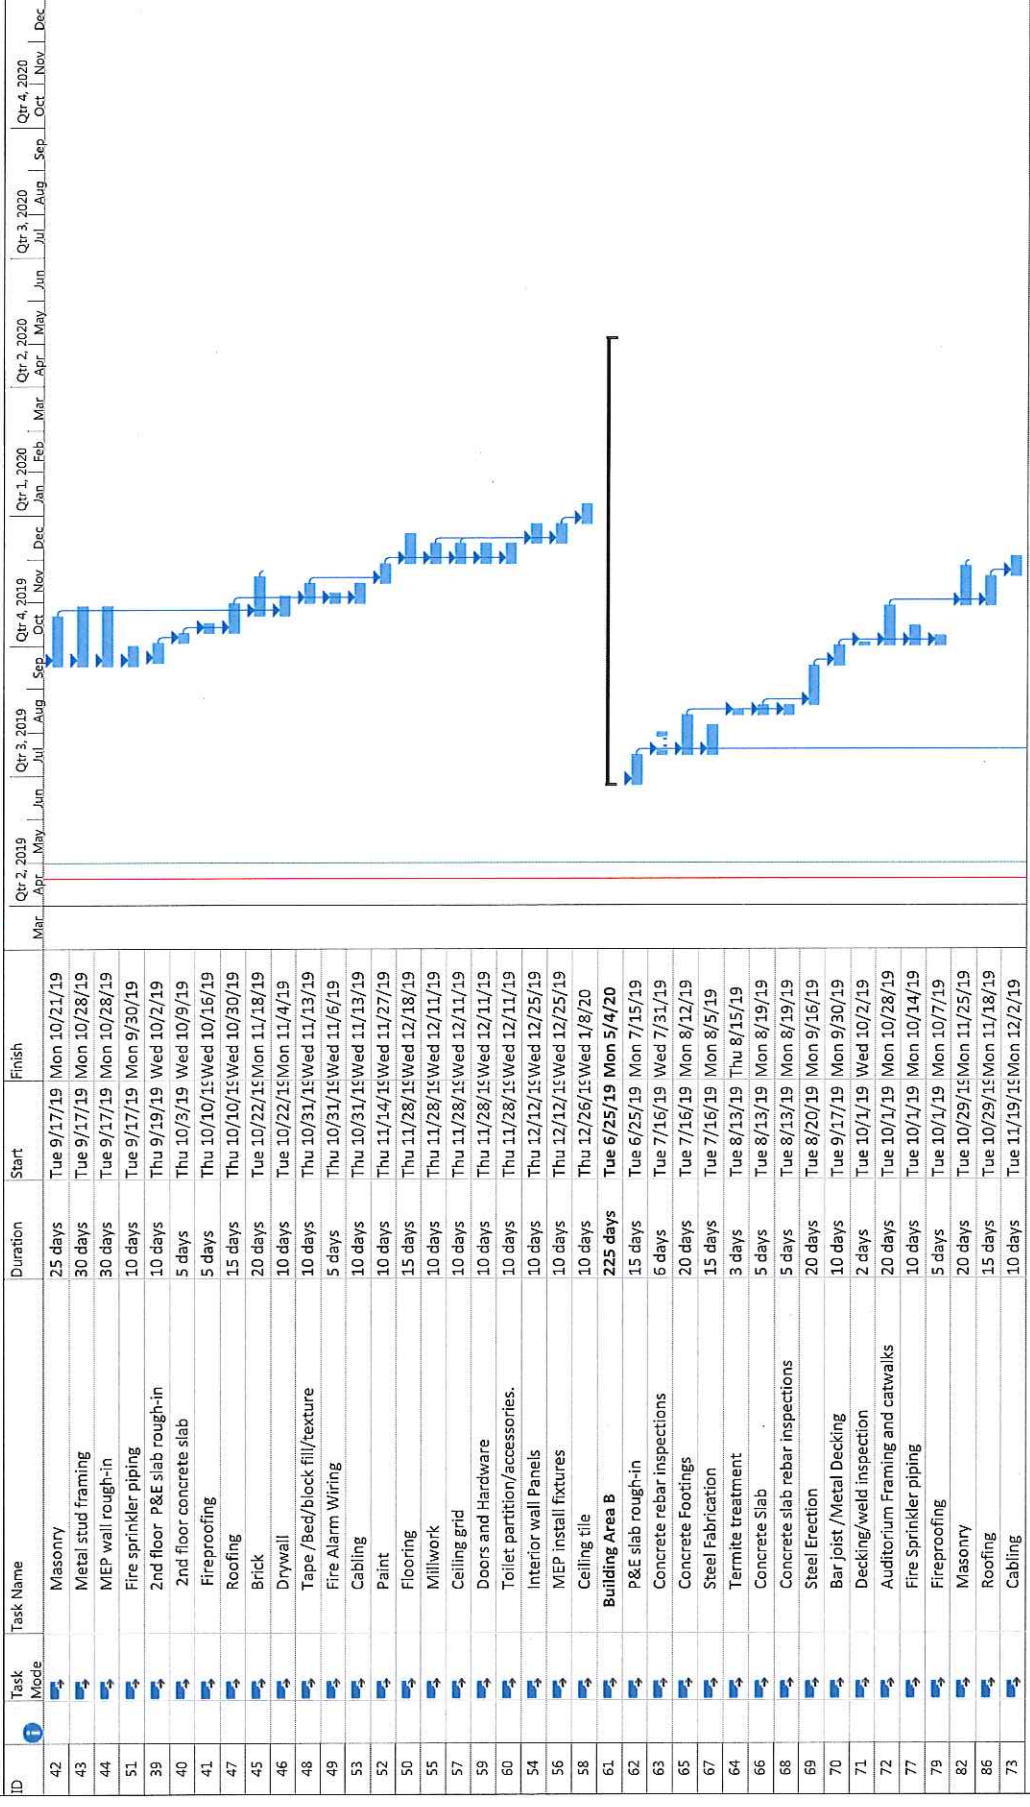


RLM General Contractors



Gilmer ISD High School

850 Buffalo Street

Gilmer, Tx 75644

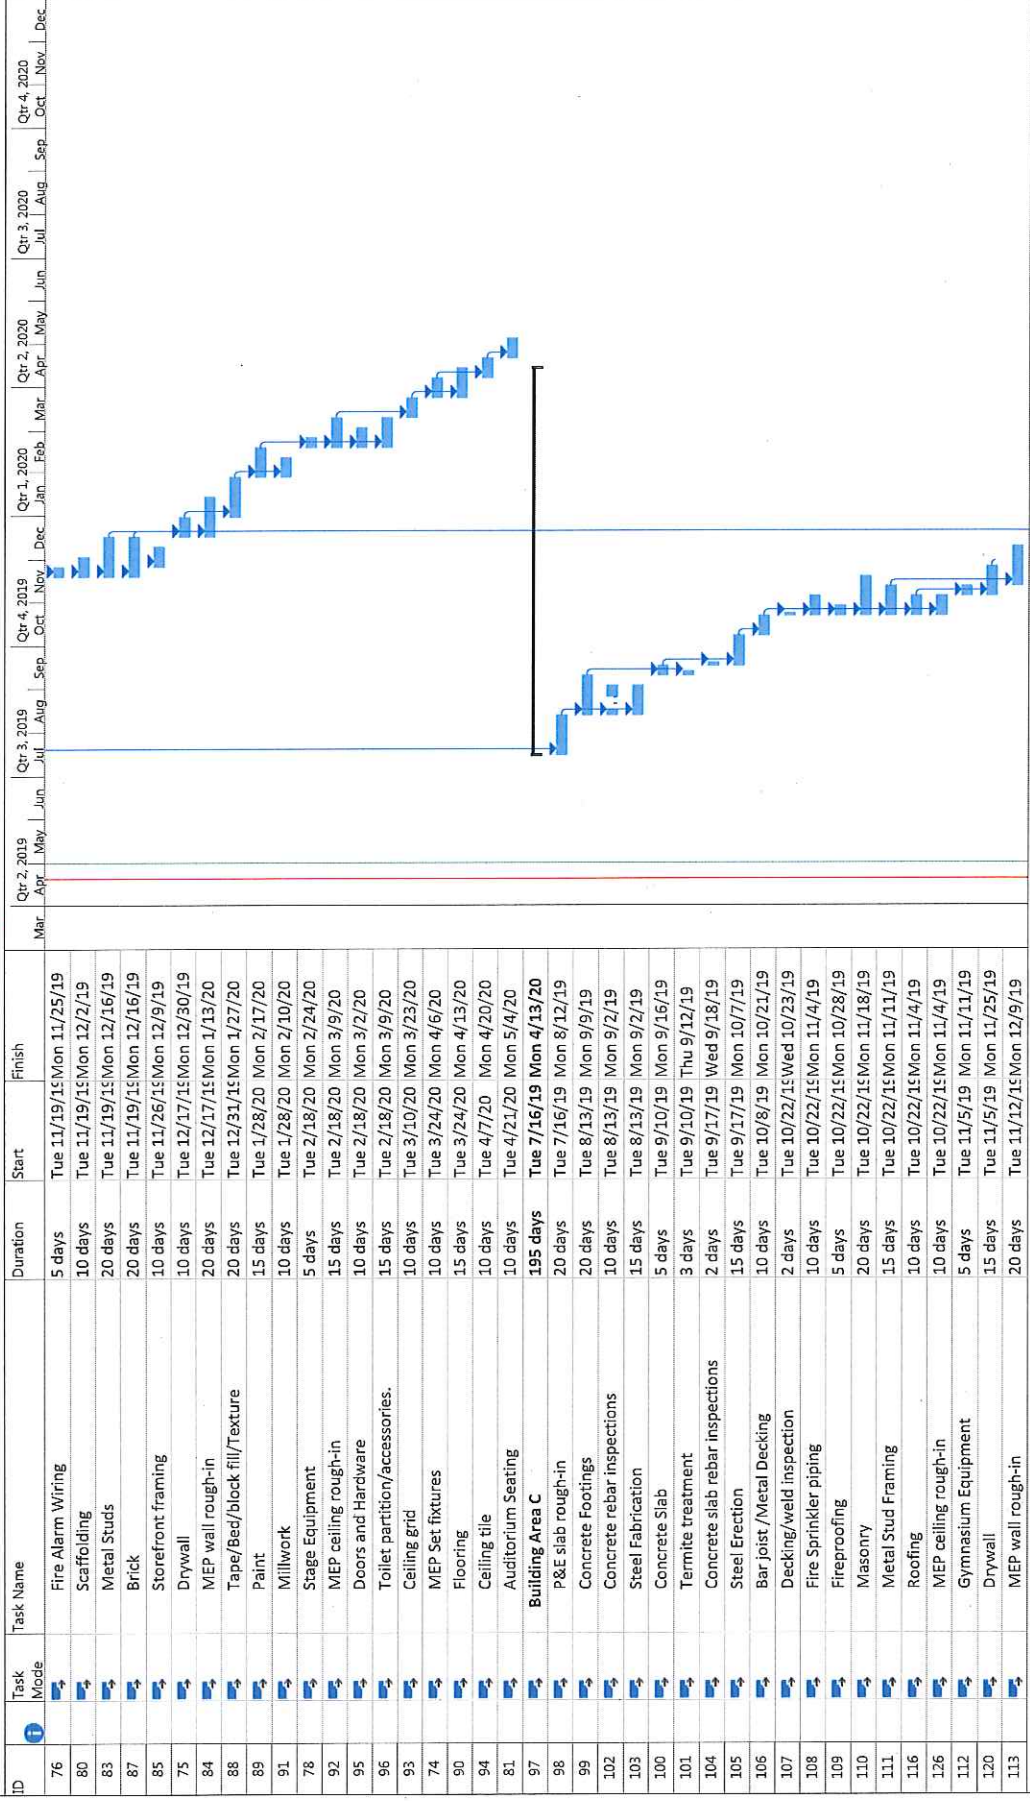


RLM General Contractors



Gilmer ISD High School

850 Buffalo Street
Gilmer, Tx 75644

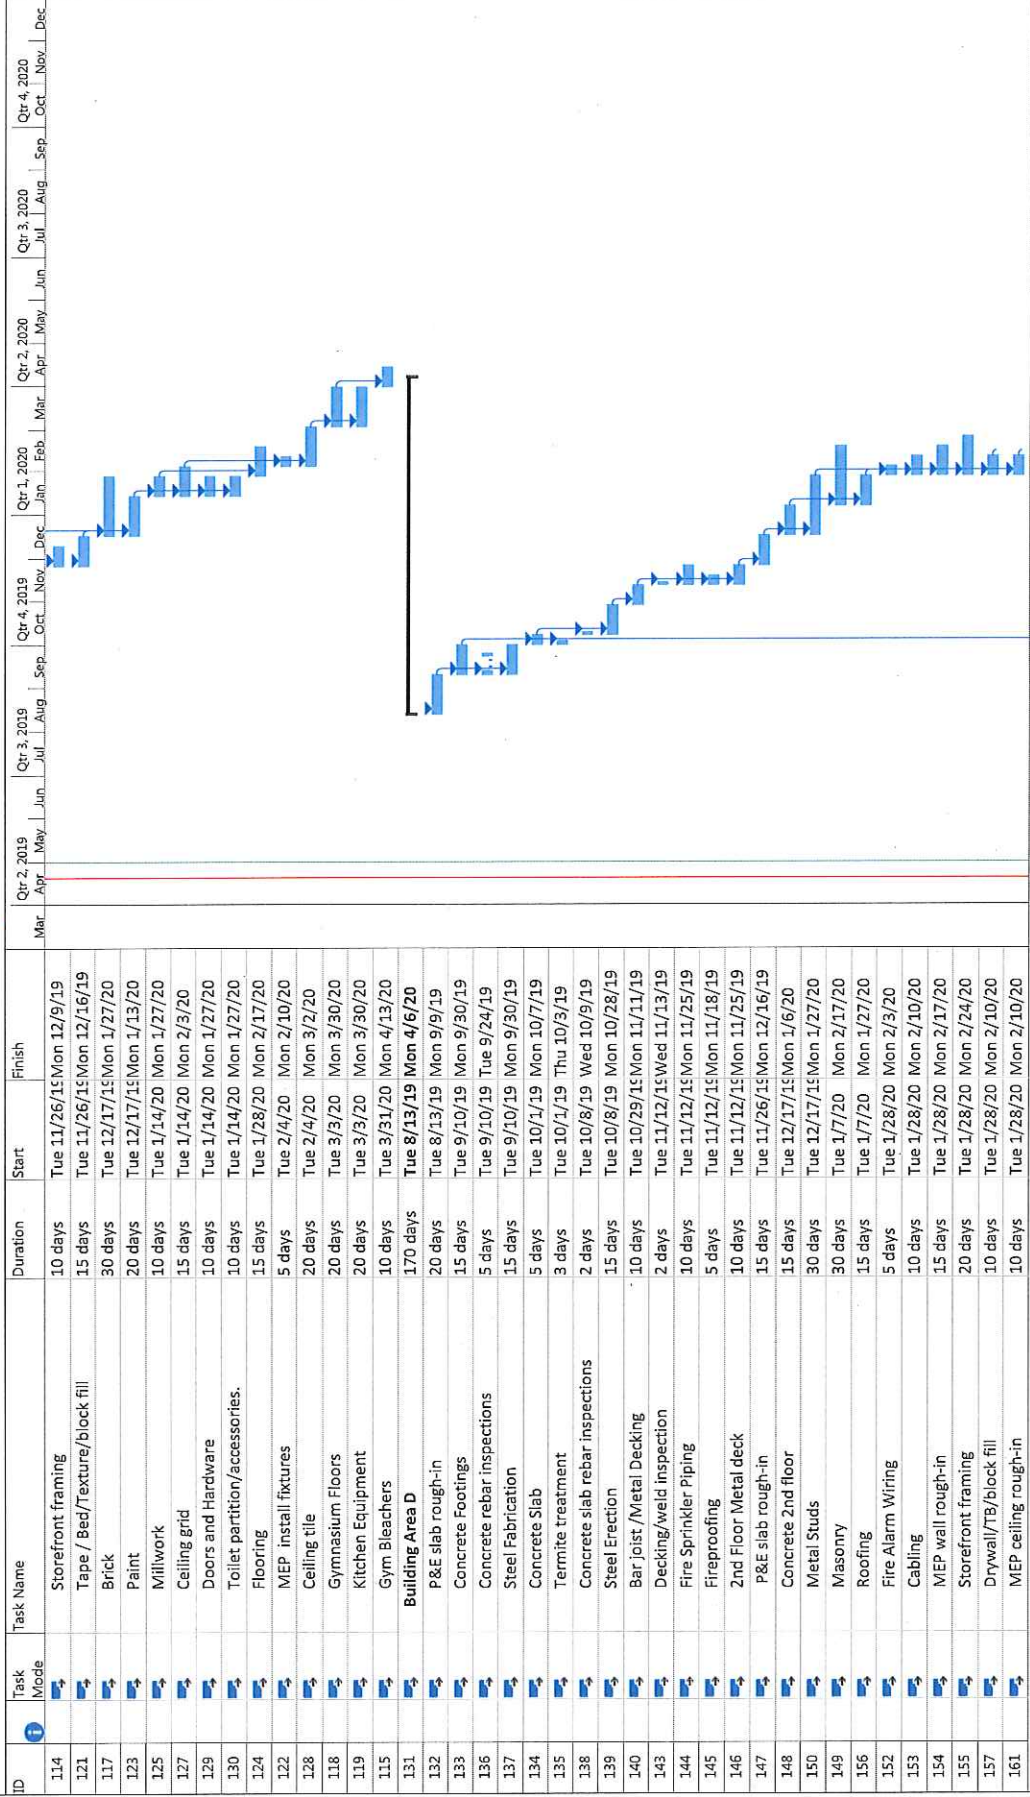


RLM General Contractors



Gilmer ISD High School

850 Buffalo Street
Gilmer, Tx 75644

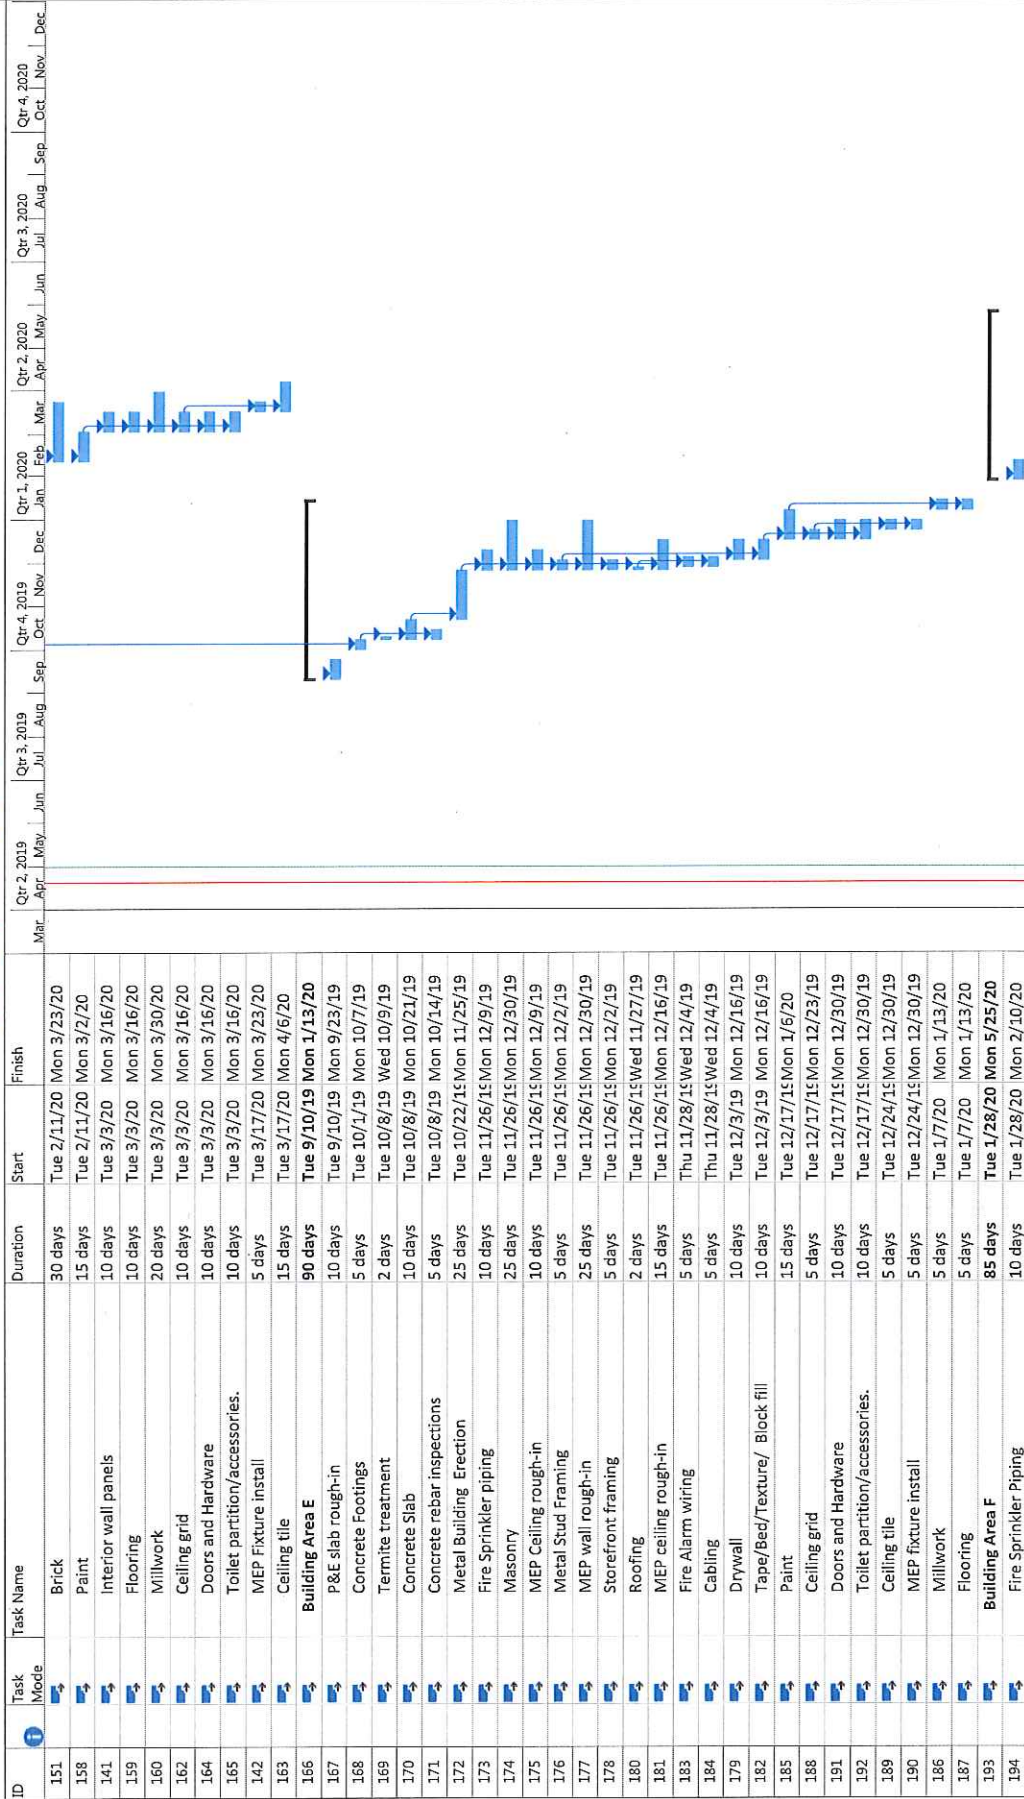


RLM General Contractors



Gilmer ISD High School

850 Buffalo Street
Gilmer, Tx 75644

ID	Task Mode	Task Name	Duration	Start	Finish
195	→	Masonry	5 days	Tue 1/28/20	Mon 2/3/20
196	→	Metal Studs	15 days	Tue 1/28/20	Mon 2/17/20
205	→	MEP ceiling rough-in	15 days	Tue 2/4/20	Mon 2/24/20
209	→	Cabling	5 days	Tue 2/4/20	Mon 2/10/20
210	→	Fire Alarm Wiring	5 days	Tue 2/4/20	Mon 2/10/20
199	→	Drywall	15 days	Tue 2/18/20	Mon 3/9/20
200	→	MEP wall rough-in	15 days	Tue 2/18/20	Mon 3/9/20
198	→	Tape/Bed/Texture/ block fill	15 days	Tue 3/10/20	Mon 3/30/20
201	→	Paint	20 days	Tue 3/31/20	Mon 4/27/20
203	→	Millwork	10 days	Tue 4/28/20	Mon 5/11/20
204	→	Science Casework	15 days	Tue 4/28/20	Mon 5/18/20
206	→	Doors and Hardware	10 days	Tue 4/28/20	Mon 5/11/20
207	→	Toilet partition/accessories.	10 days	Tue 4/28/20	Mon 5/11/20
208	→	Ceiling Grid	10 days	Tue 4/28/20	Mon 5/11/20
197	→	MEP fixture install	5 days	Tue 5/12/20	Mon 5/18/20
202	→	Ceiling tile	10 days	Tue 5/12/20	Mon 5/25/20
211	→	Building Area G	87 days	Tue 2/4/20	Wed 6/3/20
212	→	Fire Sprinkler Piping	10 days	Tue 2/4/20	Mon 2/17/20
213	→	Masonry	5 days	Tue 2/4/20	Mon 2/10/20
214	→	Metal Studs	15 days	Tue 2/4/20	Mon 2/24/20
216	→	MEP wall rough-in	10 days	Tue 2/25/20	Mon 3/9/20
215	→	Drywall/TB/block fill	10 days	Tue 3/10/20	Mon 3/23/20
217	→	Paint	15 days	Tue 3/24/20	Mon 4/13/20
218	→	Flooring	10 days	Tue 4/14/20	Mon 4/27/20
219	→	Millwork	10 days	Tue 4/14/20	Mon 4/27/20
221	→	Cabling	5 days	Tue 4/14/20	Mon 4/20/20
222	→	Fire Alarm wiring	5 days	Tue 4/14/20	Mon 4/20/20
223	→	Ceiling Grid	10 days	Tue 4/14/20	Mon 4/27/20
224	→	MEP ceiling rough-in	15 days	Tue 4/14/20	Mon 5/4/20
225	→	Doors and Hardware	10 days	Tue 4/14/20	Mon 4/27/20
226	→	Toilet partition/accessories.	10 days	Tue 4/14/20	Mon 4/27/20
220	→	MEP fixture install	5 days	Tue 4/28/20	Mon 5/4/20
227	→	Ceiling Tile	10 days	Tue 5/5/20	Mon 5/18/20
228	→	Clean and Punch	12 days	Tue 5/19/20	Wed 6/3/20
229	→	Substantial Completion	0 days	Wed 6/3/20	Wed 6/3/20
230	→	Phase 2	98 days	Wed 6/3/20	Fri 10/16/20
231	→	Demo Utilities	5 days	Wed 6/3/20	Tue 6/9/20
232	→	Demo Buildings	35 days	Wed 6/10/20	Tue 7/28/20
233	→	Remove slab/Footings	5 days	Wed 7/29/20	Tue 8/4/20

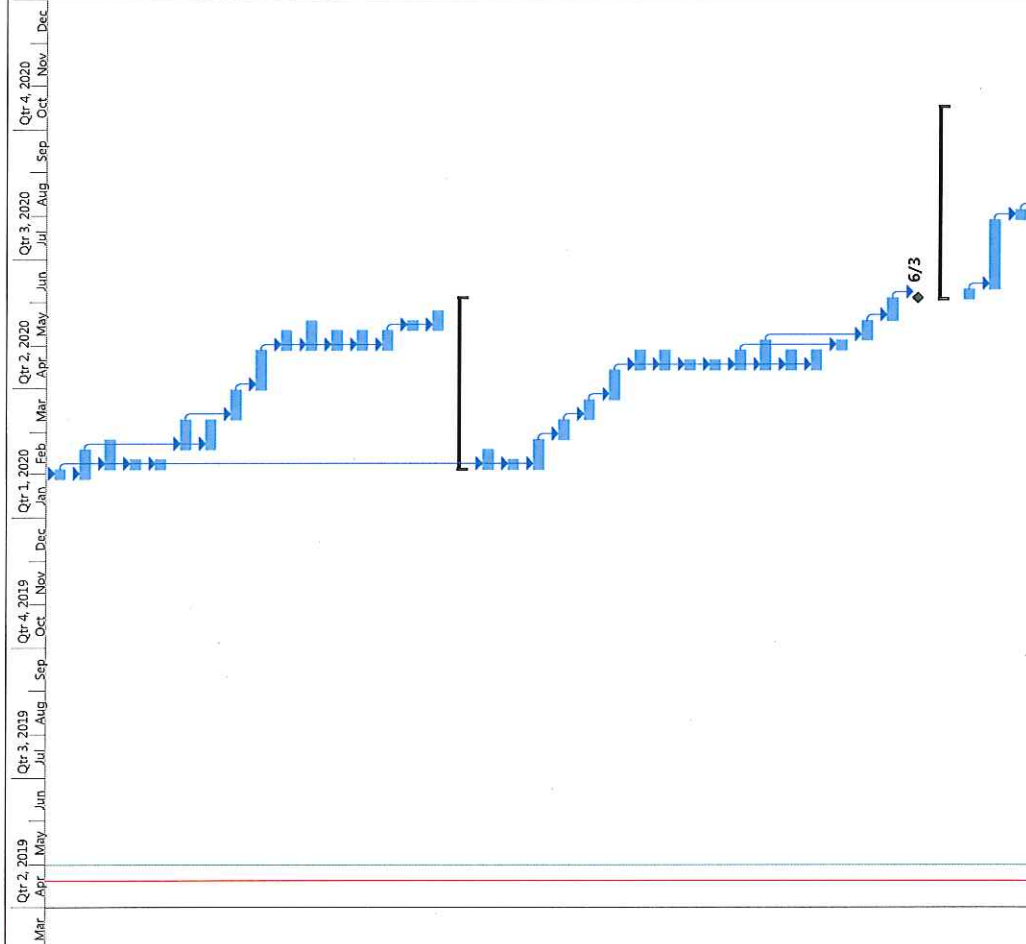

RLM General Contractors




Gilmer ISD High School

850 Buffalo Street

Gilmer, Tx 75644

ID	Task Mode	Task Name	Duration	Start	Finish
234	Task	Haul away excess dirt	15 days	Wed 8/5/20	Tue 8/25/20
235	Task	Install Storm Sewer/ water line	10 days	Wed 8/5/20	Tue 8/18/20
236	Task	Proof roll dirtwork	2 days	Wed 8/26/20	Thu 8/27/20
237	Task	Concrete sidewalks/ light pole bases	10 days	Wed 8/26/20	Tue 9/8/20
238	Task	Concrete paving	20 days	Fri 8/28/20	Thu 9/24/20
239	Task	Install light poles	5 days	Fri 8/28/20	Thu 9/3/20
240	Task	Irrigation/Landscaping	10 days	Fri 9/25/20	Thu 10/8/20
241	Task	Fences and Gates	10 days	Fri 9/25/20	Thu 10/8/20
242	Task	Parking lot striping	5 days	Fri 10/9/20	Thu 10/15/20
243	Task	Clean and Punch	1 day	Fri 10/16/20	Fri 10/16/20
244	Task	Substantial Completion	0 days	Fri 10/16/20	Fri 10/16/20

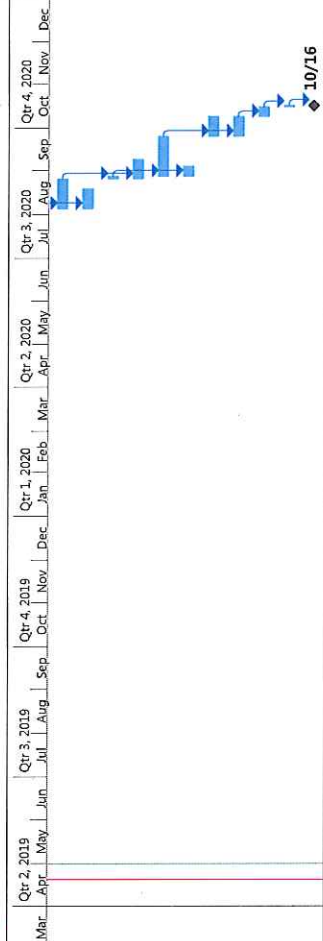

RLM General Contractors

